

FIELD REPORT

TITLE Stone Harbor Maintenance Dredging
DATE March 18, 2016
TO Jill Gougher
COPY Matt Dalon, Ben Wilk
FROM Peter Grinnell
PROJECT NO A06772

ADDRESS COWI Marine North America
20 East Clementon Rd.
Suite 201N
Gibbsboro, NJ 08026

TEL 856-248-1200
FAX 856-248-1206
WWW cowi-na.com

PAGE 1/8

Project Information

Owner: The Borough of Stone Harbor **Contractor:** Severson Environmental Services, Inc.

Daily Site Visit Information

Purpose of Visit: Observation of work in progress

Contractor: Severson Environmental Services, Inc.

Superintendent: Douglas Pike

Arrival

Time (HHMM): 0600

Weather: Sunny Clear Overcast Rain Snow

Air Temp (°F): 50

Wind: Light Moderate High **Humidity:** Dry Moderate Humid

Departure

Time (HHMM): 1400

Weather: Sunny Clear Overcast Rain Snow

Air Temp (°F): 51

Wind: Light Moderate High **Humidity:** Dry Moderate Humid

Site Locations:

Field Office:

Construction Personnel On Site: 2-3

Equipment on Site (Standby or Operating): Operational – Office Trailers (x2)

Observations: Sevensons personnel working in trailers.

Stone Harbor:

Construction Personnel On Site: 1-2

Equipment on Site (Standby or Operating): Standby – Hydraulic dredge, Boat (x1)

Observations: Dredging operations on standby.

De-watering Area:

Construction Personnel On Site: 7-8

Equipment on Site (Standby or Operating): Operational – Sump Pump (x3), Filtration System, Front End Loader, Excavator (x4), Skid-steer, Geobags (x9), Standby - De-sanding Plant, Cement Silo.

Observations: Sand blending, material disposal and cleanup in progress. Demobilization of unused equipment has begun.

Actions to be Taken: Cleanup.

Enclosures: Photographs

Photographs



Photograph 1: De-watering Area – Elevated parking lot, equipment on standby. (Looking north)



Photograph 2: Site Entrance. (Looking east)




Photograph 3: De-watering Area – Sand blending in progress. (Looking south)



Photograph 4: De-watering Area – Sand blending in progress. (Looking southwest)



Photograph 5: De-watering Area – Sand blending in progress. (Looking northwest)

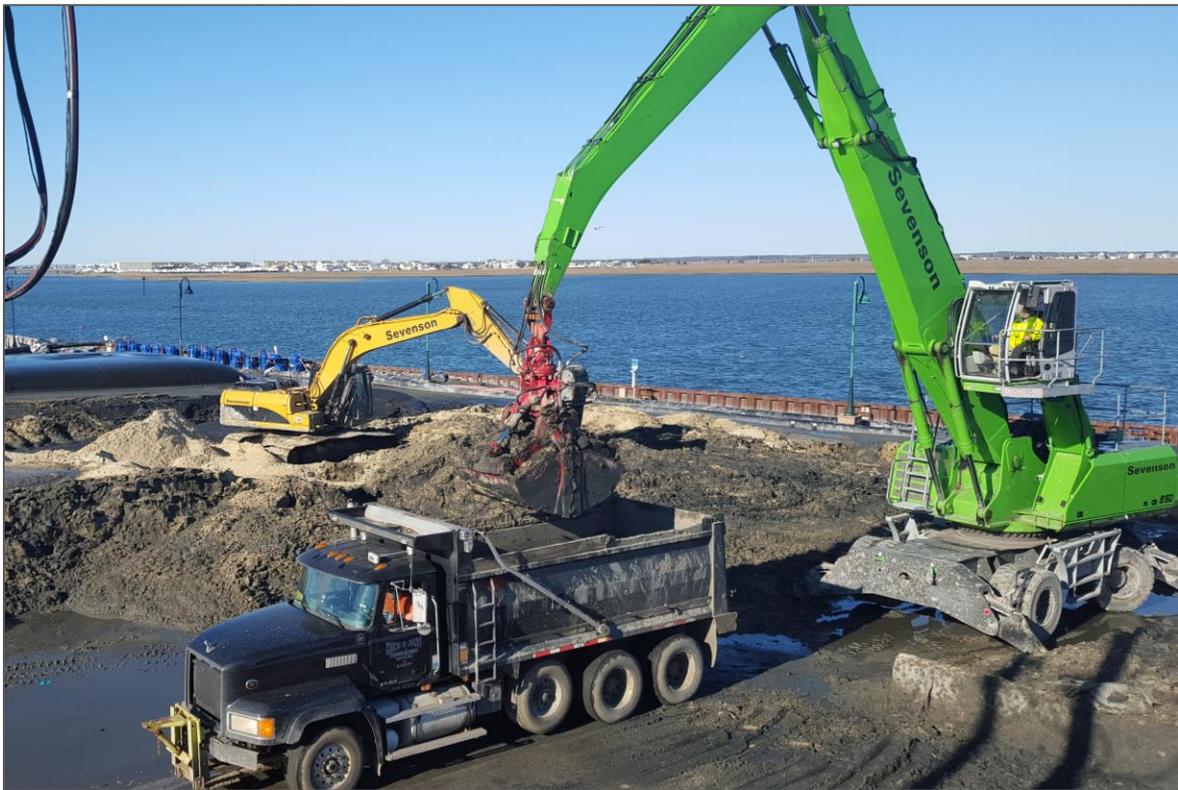

Photograph 6: De-watering Area – Material disposal in progress. (Looking southwest)



Photograph 7: De-watering Area – Sand blending in progress. (Looking west)



Photograph 8: De-watering Area – Non-operational equipment in stand-by . (Looking north)



Photograph 9: De-watering Area – Mud/slurry from geotube failure. (Looking west)



Photograph 10: De-watering Area/North Basin – Discharge pipes, mud/slurry from geotube failure. (Looking west)



Photograph 7: Stone Harbor – Hydraulic dredge on standby. (Looking south)
